



Guam SOLID WASTE RECEIVER

Quarterly Report
of
Receivership for the Government of Guam
Solid Waste Management Division
Pursuant to the Order of the
United States District Court of Guam

Presented by
Gershman, Brickner & Bratton, Inc.

August 11, 2010



Gershman, Brickner & Bratton, Inc.



Guam SOLID WASTE RECEIVER

Table of Contents

1. Layon Landfill and access road construction, construction management, design and permitting
2. Operations of the Solid Waste Management Division
3. Curbside recycling pilot project
4. Metallic and bulky item collection
5. Contract management and procurement
6. Financial issues and capital funding
7. Next steps



Gershman, Brickner & Bratton, Inc.

2

 **Guam** SOLID WASTE RECEIVER 

1. LAYON LANDFILL AND ACCESS ROAD CONSTRUCTION, CONSTRUCTION MANAGEMENT, DESIGN AND PERMITTING CONSENT DECREE PROJECTS


SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

3

 **Guam** SOLID WASTE RECEIVER 

Construction Milestones April – June 2010

- April 2010 – commenced and completed subdrain installation beneath Cells 1 and 2
- April 2010 – commenced and completed 24-inch low perm soil layer for Cells 1 and 2
- April 2010 – commenced building walls for administration, maintenance, generator and pump buildings
- April 2010 – commenced installation of utilities in entrance area and along operations road


06/25/2010 09:45


06/25/2010 13:00


SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

4

 **Guam** SOLID WASTE RECEIVER 


Construction Milestones (cont'd)

- Completed installation of wells for groundwater monitoring
- Initiated baseline monitoring sampling events at wells and surface water locations
- Commenced subbase and basecourse placement on access road
- Commenced construction of gravity sewer line along Dandan Road
- Commenced Dandan Road shoulder improvement work
- Completed detour for Talofofa Falls Resort along new access road





Gershman, Brickner & Bratton, Inc.

5

 **Guam** SOLID WASTE RECEIVER 

Layon Landfill and Access Road Construction Progress (April - June 2010)

- Major earthwork along access road completed
- Completed subbase layer along access road
- Commenced construction of all access road utilities (sewer, water, power, telephone, cable)
- Completed placement of 5,100 linear feet of sewer line along Route 4


Gershman, Brickner & Bratton, Inc.

6

 **Guam** SOLID WASTE RECEIVER 

Entrance Facilities Progress



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

April: Maintenance building

7

 **Guam** SOLID WASTE RECEIVER 

Entrance Facilities Progress



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

Early July: Maintenance building

8

 **Guam** SOLID WASTE RECEIVER 

Cell 1 and 2 Construction Progress



04.08.2010 12:12

GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

April: Installation of subdrain and low perm soil layer

9

 **Guam** SOLID WASTE RECEIVER 

Cell 1 and 2 Construction Progress





06.30.2010 12:17

GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.


June: Installation of primary liner and piping for leachate collection layer

10


 **Guam** SOLID WASTE RECEIVER 

The Liner System

↑ Six Feet + ↓

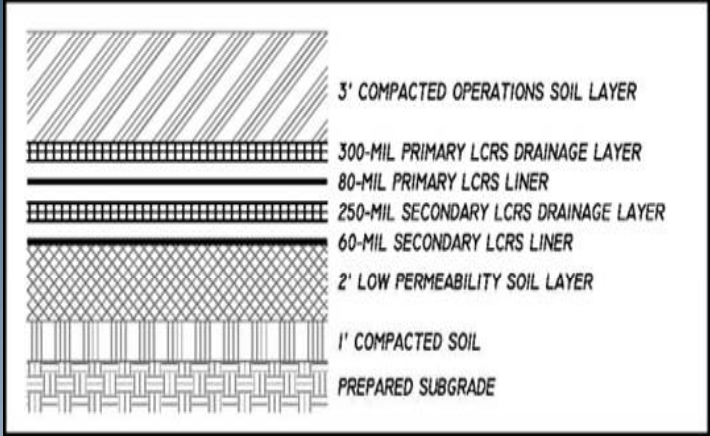

- 3' COMPACTED OPERATIONS SOIL LAYER
- 300-MIL PRIMARY LCRS DRAINAGE LAYER
- 80-MIL PRIMARY LCRS LINER
- 250-MIL SECONDARY LCRS DRAINAGE LAYER
- 60-MIL SECONDARY LCRS LINER
- 2' LOW PERMEABILITY SOIL LAYER
- 1' COMPACTED SOIL
- PREPARED SUBGRADE


Gershman, Brickner & Bratton, Inc.

11

 **Guam** SOLID WASTE RECEIVER 

Liner Installation Carefully Monitored by Independent Expert

- Third party independent expert: Vector Engineering
- Extensive expertise in landfill liner systems
- On-site oversight assures:
 - All liner materials meet specifications
 - All liner materials are properly installed
 - Conformance testing to confirm high standards




Gershman, Brickner & Bratton, Inc.

12

 **Guam** SOLID WASTE RECEIVER 

Access Road Progress




04.05.2010 12:20

April: Access Road earthwork

GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

13

 **Guam** SOLID WASTE RECEIVER 

Access Road Progress



07.03.2010 13:37

Early July: Earthwork complete, utility work ongoing

GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

14

 **Guam** SOLID WASTE RECEIVER 

Access Road Progress



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

Early July: Dandan Road improvements – gravity sewer

15

 **Guam** SOLID WASTE RECEIVER 



Access Road Progress



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

June: Sewer line construction – Route 4

16

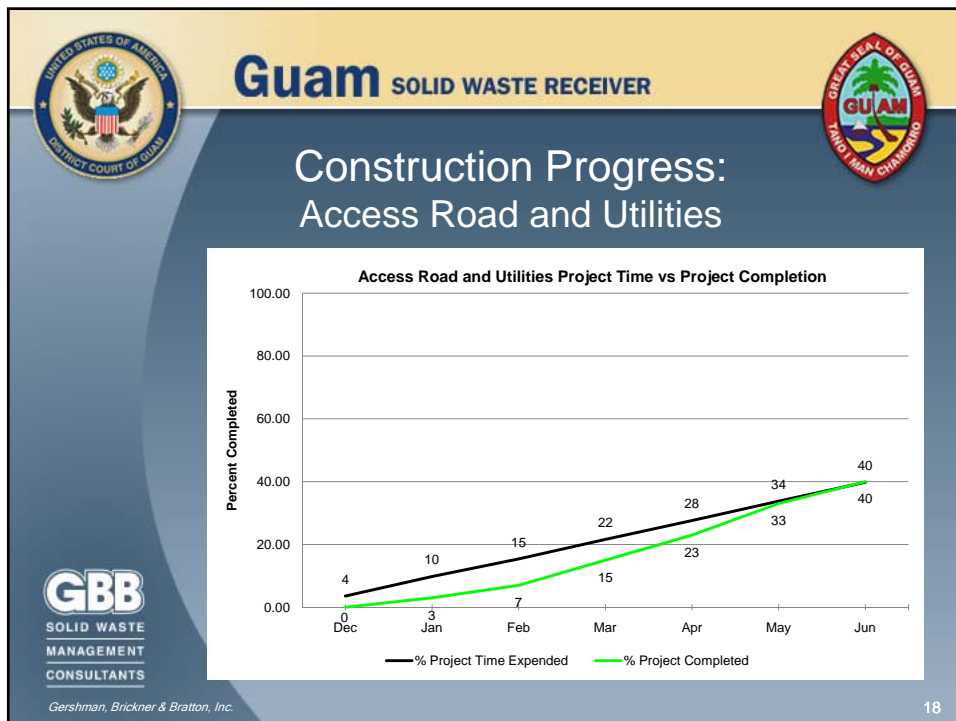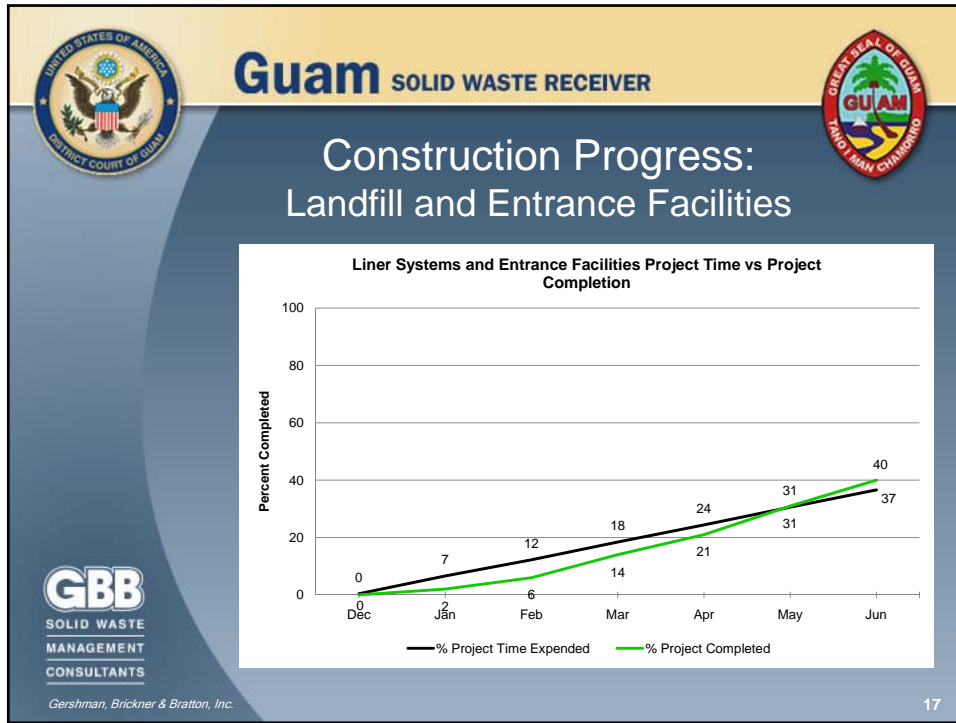

 **Guam** SOLID WASTE RECEIVER 

Construction Management

- Regular construction meetings with contractors
- Ongoing Construction Mgt. and Quality Assurance Plan implementation
- Ongoing on-site laboratory for construction quality assurance testing
- Mobilized specialty liner CQA team



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

On-site lab for quality assurance testing

19

 **Guam** SOLID WASTE RECEIVER 

Construction Management (cont'd)

- Worked closely with Mayor and village residents
- Provided environmental review and oversight of permit conditions
- Continually pushed contractors to meet project schedule
- Provided ongoing construction documentation



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

20



Guam SOLID WASTE RECEIVER

Design



- Inarajan WWTP Renovations/Monitoring:
 - Initiated design work for improvements to Inarajan WWTP
 - Conducted kickoff meetings and site visits with GEPA
 - Identified the need for monitoring plan to include a dye trace test to locate favorable marine water monitoring sites
- Continued design services support for Layon Landfill during construction to clarify design plan issues as needed



SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.


21



Guam SOLID WASTE RECEIVER

Permitting



- Ensured ongoing compliance with all permits
- Ensured construction activities were in compliance with permit conditions
- Continued bi-weekly GEPA/EPA/Receiver coordination meetings
- Initiated monthly status meeting with GEPA/EPA to discuss Consent Decree progress
- Contractors, construction management teams coordinate with GEPA and other agencies as needed



SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.


22

 **Guam** SOLID WASTE RECEIVER 



Permitting (cont'd)

Pump Station Property Zoning:

- Continued processing through Dept. of Land Management procedures
- July 13, 2010. Public Hearing held for both properties -- No concerns raised
- August 12, 2010. Anticipated GLUC meeting for final consideration



SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.


23

 **Guam** SOLID WASTE RECEIVER 



Ordot Dump Closure

- Continued to implement interim filling plan
- Tracked air space volume usage
- Met with GEPA/EPA on April 30 and June 28 to discuss framework for moving forward with dump closure




SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.


24



Guam SOLID WASTE RECEIVER



Ordot Dump Closure (cont'd)

- June 10, 2010. Receiver requested GovGuam and EPA provide regulatory/permit guidance
- July 1, 2010. EPA provided a detailed response to our request for regulatory/permit guidance
- EPA also provided specific comments to the draft RCRA environmental investigation SOW
- July 31 2010. GovGuam and GEPA provided very general response to our request for regulatory/permit guidance



Gershman, Brickner & Bratton, Inc.


25



Guam SOLID WASTE RECEIVER



Schedule for Closing of Ordot Dump

- Consent Decree outlines a 45-month schedule for final closure of the Ordot Dump
- Receiver anticipates a shorter schedule
- Initial planning and design must be completed before a realistic schedule is established



Gershman, Brickner & Bratton, Inc.

26

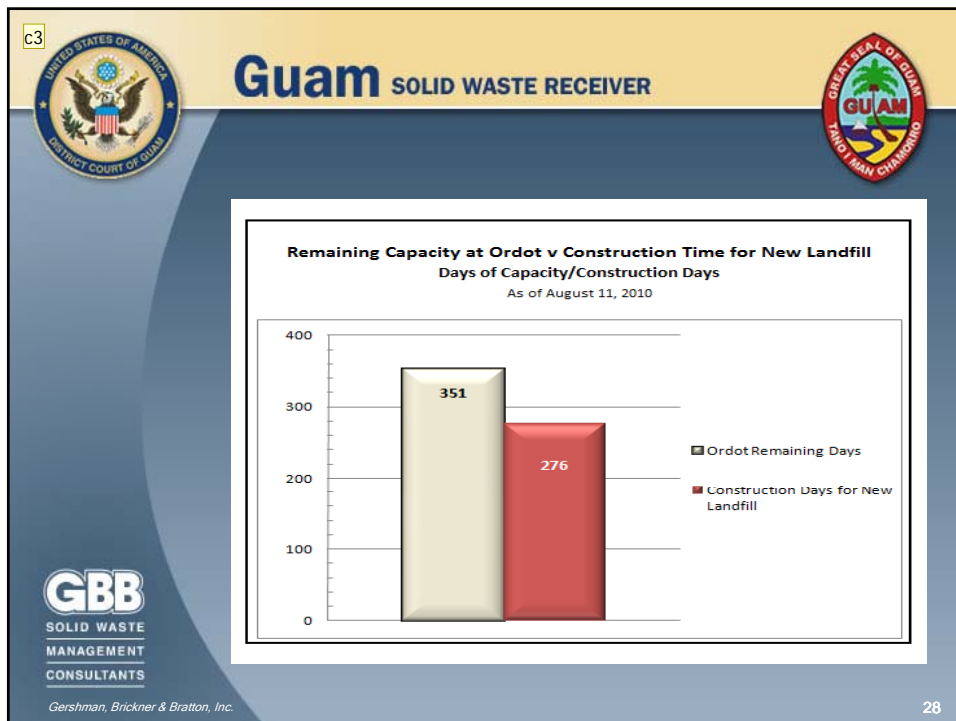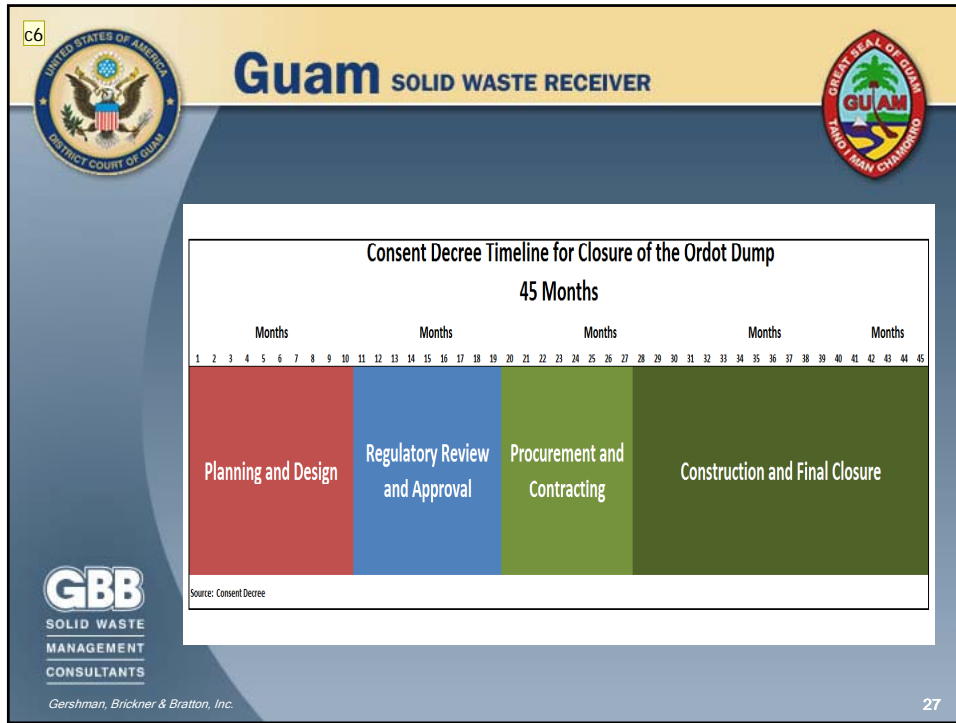

Slide 27

c6

REMAINING DAYS FROM APRIL 8 IS

475 DAYS

clund, 3/21/2010

Slide 28

c3

REMAINING DAYS FROM APRIL 8 IS

475 DAYS

clund, 3/21/2010



Guam SOLID WASTE RECEIVER

2. OPERATIONS OF THE SOLID WASTE MANAGEMENT DIVISION



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.

29



Guam SOLID WASTE RECEIVER

Trash Cart Rollout




- Registration for trash cart system completed
- 19,416 customers as of July 30 – 60% increase over 12,080 customers in March 2008
- Customers continue to sign up for service



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.

30

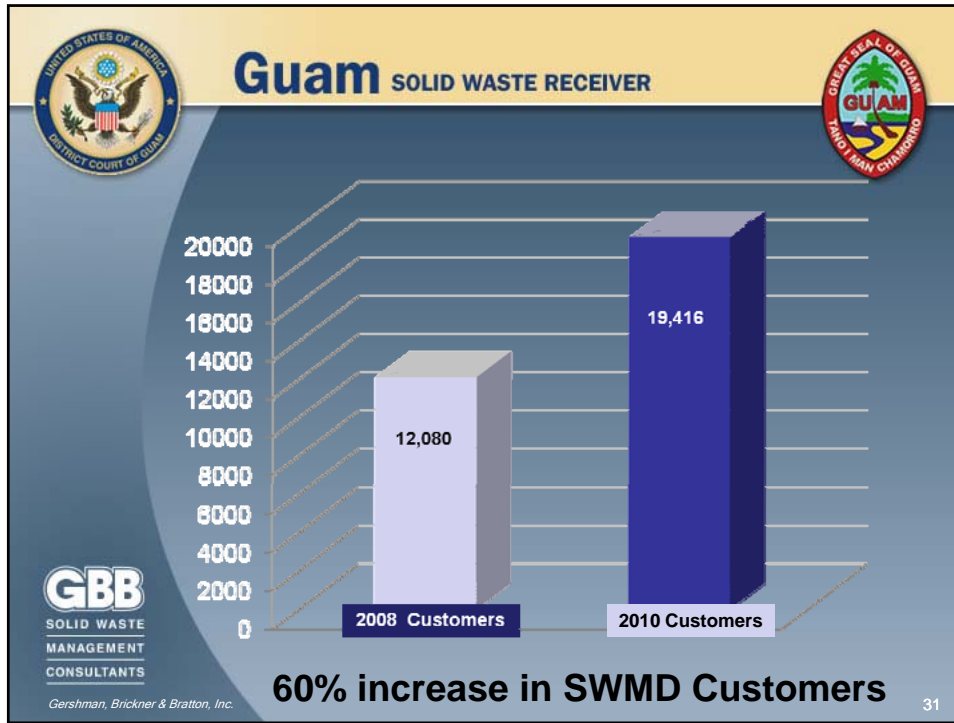

Guam SOLID WASTE RECEIVER

Residential Collection

Benefits of Carts

- Uniform collection system
- Less rainwater in trash due to covers
- Improved neighborhood aesthetics
- Monitored with RFID tags

No uniformity in old system

GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

32



Guam

SOLID WASTE RECEIVER



Cart Repairs


- Small number (0.74%) of carts have required repairs
- Types of repairs: axles, wheels, lids, RFID tags
- Rough terrain is primary cause






Gershman, Brickner & Bratton, Inc.

33



Guam


SOLID WASTE RECEIVER



New Customer Service Software



- Allows SWMD staff to categorize calls
- 910 calls, April – June
- Customer complaints declined as a % of customer base
- Other calls: When will my cart come? (40%); requests to register (8%); non-compliance issues (no tags on bags, banned materials, etc.)

Month	Customer Complaints Missed or Late Trash Collection			
	2009		2010	
	Complaints	% of Customers	Complaints	% of Customers
April	54	0.43%	74	0.40%
May	65	0.52%	73	0.40%
June	56	0.44%	85	0.44%



Gershman, Brickner & Bratton, Inc.


34



Guam SOLID WASTE RECEIVER

Operations Improvements

- SWMD collections unit reorganized to allow faster allocation of staff resources to where they are needed
- Ordot Dump managed so as to minimize rental equipment (\$464/day vs. \$11,000/day in 2008) and reduce flies and odors
- SWMD has 65 workers: 56 employees, 7 temporary staff and 2 contractors, 35% reduction from 99 in March 2008; productivity up



SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.

35



Guam SOLID WASTE RECEIVER

Court Ordered Cleanup of DPW Compound

- Some improvements have occurred in the area adjacent to SWMD
- Contracts are in place to remove drums
- Receivership has provided funding for the removal of drums
- Funds to be reimbursed to Citibank Trust Account in October per the Court's Order



SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.

36

 **Guam** SOLID WASTE RECEIVER 

Court Ordered Cleanup of DPW Compound

- The Court was informed in June that the tires and abandoned vehicles had been removed
- This is not accurate
- Tires and abandoned vehicles were removed from the immediate vicinity of the SWMD but remain on the compound





Gershman, Brickner & Bratton, Inc.

37

 **Guam** SOLID WASTE RECEIVER 



Photos of DPW Compound taken on July 30, 2010







Gershman, Brickner & Bratton, Inc.

38



Guam SOLID WASTE RECEIVER

3. CURBSIDE RECYCLING PILOT PROJECT



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.

39



Guam SOLID WASTE RECEIVER

Curbside Recycling Pilot Project

- Background: October 2008, Receiver discussed with Court a possible pilot recycling program
- With trash cart delivery program in place, staff and vehicles are available to move forward



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.

40

 **Guam** SOLID WASTE RECEIVER 

Curbside Recycling Pilot Project (cont'd)

Description:

- 1,000 single family homes, clustered in villages throughout Guam for collection efficiency
- Each home to receive a recycling cart with green lid
- Recycling and trash collection on same day
- Recyclables delivered to processor on Guam
- Recyclables to be weighed, processed, baled and shipped off island



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

41

 **Guam** SOLID WASTE RECEIVER 

Curbside Recycling Pilot Project (cont'd)



Materials collected:

- Fiber/cardboard, paper
- Aluminum and metal cans
- Plastic bottles and jars #1 (PET) and #2 (HDPE)



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.


42



Guam SOLID WASTE RECEIVER



Curbside Recycling Pilot Project (cont'd)

- Program to be phased in, from north to central to south areas
- To test costs and efficiencies at different collection intervals, homes to be divided into 3 groups:
 - Weekly recycling collection
 - Every other week recycling collection
 - Monthly collection



Gershman, Brickner & Bratton, Inc.

43




Guam SOLID WASTE RECEIVER

Curbside Recycling Pilot Project (cont'd)

Program evaluation based on:

1. Participation in recycling – assessed through periodic waste characterization study of 50 households in pilot
2. Contamination/trash in recycling cart
3. Weight of material collected
4. Cost of providing services; revenue offsets

Results will be used to evaluate the future direction of curbside recycling collection



Gershman, Brickner & Bratton, Inc.

44

 **Guam** SOLID WASTE RECEIVER 

4. METALLIC AND BULKY ITEM COLLECTION


SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

45

 **Guam** SOLID WASTE RECEIVER 

Metallic and Bulky Item Collection

- 2008: Court approved a collection system for metallic and bulky items
- With trash cart system in place, Receiver and SWMD have developed a plan for new collection service




SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

46

 **Guam** SOLID WASTE RECEIVER 

Outline of Metallic and Bulky Item Collection



Items collected

- Metallic: appliances, hot water tanks
- Bulky items: sofas, mattresses, furniture



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

47

 **Guam** SOLID WASTE RECEIVER 



Outline of Metallic and Bulky Item Collection (cont'd)

SWMD residential customers:

- Receive 2 free collections a year
- Additional collections for a set fee
- Fee applied to monthly invoice
- Up to 5 items/pickup


GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS
Gershman, Brickner & Bratton, Inc.

48



 **Guam** SOLID WASTE RECEIVER 

Outline of Metallic and Bulky Item Collection (cont'd)

- Options for residents and businesses that are not SWMD residential customers:
 - Metallic items go to scrap dealers
 - Non-metallic bulky items to be accepted at Ordot Dump until new landfill opens
 - When landfill opens: 2 transfer stations (one in North and one in Malojloj) will receive non-metallic bulky items
- Receiver to evaluate extending the bulky item program for non-customers at a later time



Gershman, Brickner & Bratton, Inc.


49

 **Guam** SOLID WASTE RECEIVER 

Equipment and Staff Needed for Metallic and Bulky Item Collection Program

- Original estimate -- \$553,500
 - 2 knuckle-boom trucks
 - 3 trailers
 - 2 transport trucks
- Revised estimate -- \$305,000
 - 2 knuckle-boom grapple hook trucks
- SWMD staff operating trucks will be re-assigned from daily trash routes that have been consolidated




Gershman, Brickner & Bratton, Inc.

50



Guam SOLID WASTE RECEIVER



5. CONTRACT MANAGEMENT AND PROCUREMENT



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.


51



Guam SOLID WASTE RECEIVER

Activity during the Quarter

- Management of Consent Decree contracts
- Preparing for procurements for:
 - Commercial Transfer Station
 - Operator of Layon Landfill
 - Initial work to begin closure of Ordot Dump



GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.

52



Guam SOLID WASTE RECEIVER

Current Contracts



Table 1

All contracts to complete Layon Landfill are now in place.

Consent Decree Contracts as of June 30, 2010

Contractor	Purpose of Contract	Amount of Contract	Citibank Trust Account Expenditures	Work Status
Maeda Pacific Corporation	Layon Landfill - Construction of Landfill Operations Road and Mass Grading for Cells 1 and 2	\$ 10,045,245	\$ 9,542,983	Close-Out Phase
Core Tech International	Layon Landfill - Construction of Access Road and Utility Improvements for Community	\$26,832,053	\$ 3,150,576	On-going
Black Construction Corporation	Layon Landfill - Construction of Entrance Facilities and Cells 1 and 2	\$22,053,298	\$ 3,785,301	On-going
EA Engineering, Science & Technology, Inc.	Groundwater Quality Monitoring Services	\$ 857,750	\$ 46,220	On-going
TG Engineers, PC	Layon Landfill - Design and Engineering Services	\$ 9,522,562	\$ 1,192,022	On-going
Winzler & Kelly	Construction Management Services for Consent Decree projects	\$ 3,875,284	\$ 995,985	On-going
Shaw Environmental, Inc.	Technical Assistance	\$ 305,347	\$ 1,371	On-going
Pacific Human Resources Services, Inc.	Temporary Staffing Services for the Solid Waste Management Division	Indefinite	\$ 233,143	On-going
Alpine Technology, Inc.	Customer Service Software	\$ 240,078	\$ 181,708	On-going
Far East Equipment	New Trucks, Roll-off containers and Trash Carts	Gov Guam Purchase Orders	\$ 2,017,588	On-going
G4 Security Services of Guam	Security Services for the Solid Waste Compound	Indefinite	\$ 16,904	Closed
Pacific Island Security Agency	Security Services for the Solid Waste Compound (replaced G4 Security Services of Guam)	Indefinite	\$ 32,774	On-going

Note: Does not include retainage or expenditures directly paid by the Government of Guam. All contracts are inclusive of change orders approved through June 30, 2010.



Gershman, Brickner & Bratton, Inc.

53



Guam SOLID WASTE RECEIVER

Commercial Transfer Station



- Facility will consolidate waste from residential and business customers into larger truckloads for transport to Layon Landfill
 - Improves efficiency, reduces cost, decreases truck traffic near landfill
- A permitted private facility already exists in Guam
- To assess interest of this facility and others, Receiver issued Request for Expression of Interest on July 12
- Next steps will be determined by results of RFEI



Gershman, Brickner & Bratton, Inc.

54



Guam SOLID WASTE RECEIVER



Operator for Layon Landfill

- Receiver developed initial RFP for the operator
- RFP reviewed by Office of the Attorney General
- RFP to be finalized in late August, early September
- Contract to be finalized in early 2011



Gershman, Brickner & Bratton, Inc.


55



Guam SOLID WASTE RECEIVER

Closure of Ordot Dump

- April: Receiver submitted draft scope of work for consultants who will:
 - Investigate environmental damage from Dump
 - Recommend remedial action
- EPA and GEPA have provided suggestions
- Receiver to revise scope of work and proceed with initial procurement this fall



Gershman, Brickner & Bratton, Inc.

56



Guam SOLID WASTE RECEIVER



GovGuam Solid Waste RFP

- Funded through the Office of Economic Assistance of the Department of Defense
- **Scope of Work:**
 - Analyze alternative waste management for household waste, household hazardous waste, commercial solid waste, industrial solid waste applicable, thus reducing the amount of waste going into the Layon Landfill
 - Evaluate each alternative
 - Identify costs associated to plan, procure, build, operate and maintain preferred alternatives
 - Identify proposed strategy to implement
 - Provide draft legislation for implementation of preferred alternatives when applicable
- Objectives and purpose of the proposed work are unclear to us
- Funding may be more effectively applied to enhance recycling




Gershman, Brickner & Bratton, Inc.

57




Guam SOLID WASTE RECEIVER


6. FINANCIAL ISSUES AND CAPITAL FUNDING



Gershman, Brickner & Bratton, Inc.



Guam SOLID WASTE RECEIVER



Operating Results FY2010


Expenditures: 55% Below Approved Budget

- Payroll/benefits – 34.8% under budget
- Non-personnel expenses – 68.2% under budget

Solid Waste Management Division
Operating Budget
FY 2010
October 1, 2009 to June 30, 2010


Item	FY 2009 Actual Expenditures	FY 2010 Approved Budget to Date	FY 2010 Actual Spending* to Date	% over budget Budget
Personnel Expenses:				
Regular Salaries	\$ 1,503,710	\$1,653,284	\$1,121,297	-32.2%
Overtime/Special Pay	\$ 22,911	\$261,413	\$151,033	-42.2%
Benefits	\$ 577,238	\$503,491	\$303,192	-39.8%
Sub-total	\$2,503,859	\$2,418,188	\$1,575,522	-34.8%
Non-Personnel Expenses:				
Travel	\$ 3,545	\$0	\$0	N/A
Contractual Services	\$ 1,265,160	\$2,825,101	\$778,813	-72.4%
Supplies and Materials	\$ 442,188	\$503,380	\$339,908	-32.5%
Equipment	\$ 4,599	\$56,000	\$3,761	-94.3%
Utilities - Power and Water	\$ 16,860	\$65,375	\$18,866	-71.1%
Communications	\$ 17,703	\$12,042	\$10,838	-10.0%
Capital Outlay	\$ 221,738	\$185,000	\$9,150	-95.1%
Miscellaneous	\$ 1,256	\$7,000	\$2,004	-71.4%
Sub-total	\$ 1,973,048	\$ 3,663,899	\$ 1,163,341	-68.2%
Grand total	\$ 4,476,907	\$6,082,086	\$2,738,863	-55.0%

*Does not include encumbrances




Gershman, Brickner & Bratton, Inc.

59



Guam SOLID WASTE RECEIVER




Revenue Billed and Collected

SWMD Revenue Billed / Collected
October 1 through June 30
FY 2010



Customer Class	Billed	Collected	%
Commercial	\$ 5,329,878	\$ 4,455,130	83.6%
Residential	\$ 1,245,235	\$ 1,173,782	94.3%
Government	\$ 216,716	\$ 13,163	6.1%
Total	\$ 6,791,829	\$ 5,642,075	83.1%

Note: Amount collected is on a cash basis. Transfer Stations are included in the residential category.



Gershman, Brickner & Bratton, Inc.

60


Guam SOLID WASTE RECEIVER

SWMD Fund Balance FY2010

**Solid Waste Management Division
Fund Balance
30-Jun-10
(Unaudited)**



Elements of Fund Balance	Amount
Fund Balance @ 9/30/09	\$ (182,596)
Revenue FY 2010	\$ 6,791,829
Expenses FY 2010	<u>\$ 2,738,863</u>
Excess (Deficit) FY 2010	\$ 4,052,966
Fund Balance @ 6/30/10	<u>\$ 3,870,370</u>

Note: Revenue is on accrual basis.



Gershman, Brickner & Bratton, Inc.


61

Guam SOLID WASTE RECEIVER


New Solid Waste Billing Process for Residential Customers

- In operation for 6 months
- SWMD staff managing system well
- Plans underway to integrate billing for commercial customers
- Working with GovGuam to reconcile with the accounting system
- Customers have option to pay using GuamPay or mail payment to SWMD



Gershman, Brickner & Bratton, Inc.

62

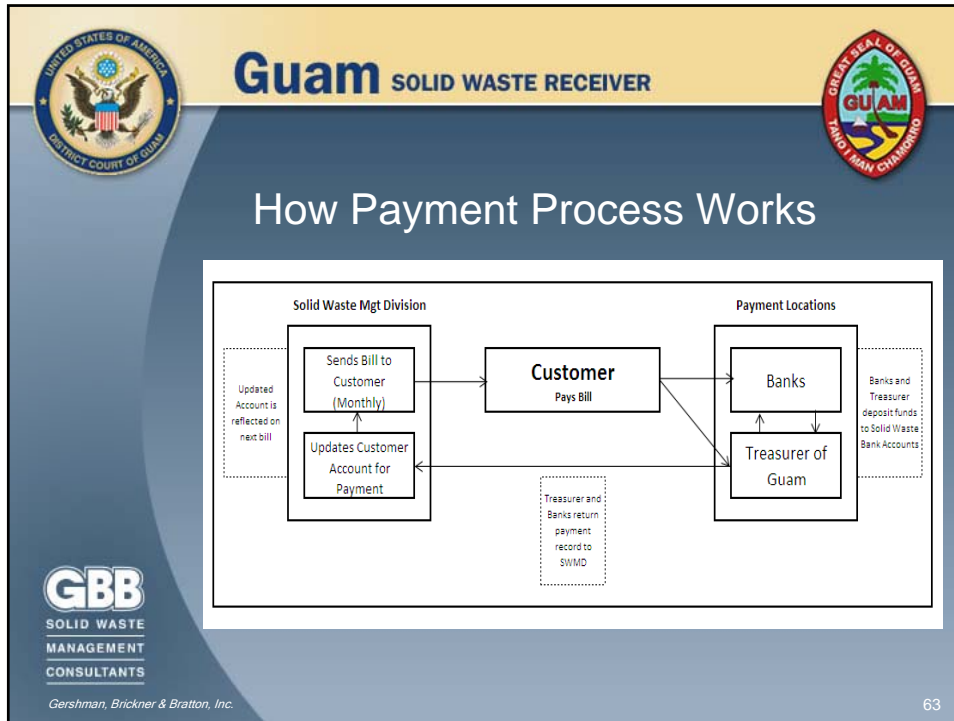

Guam SOLID WASTE RECEIVER

Problems with Payments through Treasurer of Guam


Issues:

- Information sent to SWMD about customer payments made through Treasurer of Guam is delayed
- Treasurer has interrupted access to online and credit card payments without notice
- Other errors make it difficult to update customer accounts

Recommendation: Receiver contracts with a commercial bank on Guam to receive all customer payments, including mailed payments, on behalf of SWMD and deposit funds directly to SWMD's bank account. Bank would transmit information about payments daily and develop updates for those who pay using GuamPay.


Logos for the United States of America District Court of Guam and the Great Seal of Guam are present. The GBB Solid Waste Management Consultants logo is also included.

Gershman, Brickner & Bratton, Inc. 64




Guam

SOLID WASTE RECEIVER




Delinquent Customers

- Over 80% of SWMD Customers pay on time and in full
- 14% (2,600) of SWMD customers currently delinquent
- An additional 4% (900) of customers are late with payments and close to delinquency
- Receiver asks Court to approve policy to address delinquencies
 - After 30 days a reminder call from Customer Service
 - After 60 days notification that unless account is paid in full within 30 days, service ends and cart is recovered
 - To restore service customer must pay sum due, plus prepayment of one month and \$50 for restoring service
 - If delinquent account is turned over to a collection agency, to restore service, customer must pay all sums due, plus prepayment of one month, plus \$100 fee
 - Customers are responsible for cost of carts (damaged or unrecovered)




Gershman, Brickner & Bratton, Inc.

65



Guam

SOLID WASTE RECEIVER




Updated Capital Funding Requirements

- No changes since April Report to Court
- Estimated savings in cost of Layon Landfill: approx. \$21 million

Layon Landfill and Related Consent Decree Projects
As of June 30, 2010



Capital Budget Item	Approved Budget	Actual Contract Amount	Revised Budget		Savings
			Reserve for Change Orders	Revised Estimate	
Layon Landfill	\$ 81,022,300	\$ 58,930,596	\$ 3,980,443	\$62,911,039	\$18,111,261
Construction Management - Layon	\$ 7,316,400	\$ 3,875,284	\$ 1,550,114	\$ 5,425,398	\$ 1,891,002
WWTP Expansion & Leachate Sewer and Pre-Treatment - Layon	\$ 11,023,000			\$11,023,000	\$ -
Landfill Equipment	\$ 6,380,000			\$ 5,217,413	\$ 1,162,585
Transfer Station/WWTP	\$ 3,505,000			\$ 3,505,000	\$ -
Transfer Station Equipment	\$ 2,440,000			\$ 2,403,000	\$ 35,000
Operating Equipment*	\$ 5,941,400	\$ 2,199,297		\$ 5,941,400	\$ -
Total New Construction/Equipment	\$ 119,630,100	\$ 65,005,177	\$ 5,530,557	\$98,430,252	\$21,199,848

*Actual contract amounts are equipment purchases completed as of June 30, 2010.



Gershman, Brickner & Bratton, Inc.


66

Guam SOLID WASTE RECEIVER

Status of Citibank Trustee Account

- Primary Citibank account used for Consent Decree purposes authorized by the Court that cannot be charged to construction subaccount
- GovGuam replenished construction account in April with deposit of \$11,616,263.70
- Details of all transactions in both accounts are included in the Report to the Court



Gershman, Brickner & Bratton, Inc.

67




Guam SOLID WASTE RECEIVER

Citibank Trustee Account As of June 30, 2010



Account	Balance
Primary Account	\$3,787,021.92
Construction Subaccount	\$10,967,238.46

Note: Detailed transactions are included in Tabs 6 and 7 of the narrative report.



Gershman, Brickner & Bratton, Inc.


68



Guam SOLID WASTE RECEIVER



Status of USDA Loan/Grant

- Receiver assisted GovGuam and USDA as they worked to finalize loan/grant
- Most issues we raised in October, January and April reports remained outstanding
- Contract requirements for “Buy American” and “Davis-Bacon” provisions are important in landfill contracts now in close-out or almost half completed
- Governor Camacho has now declined the USDA Loan/Grant for reasons not related to the Court or Receiver



Gershman, Brickner & Bratton, Inc.


69



Guam SOLID WASTE RECEIVER



Preliminary Rate Recommendations for PUC

- Receiver has updated preliminary rates using new information and data available since April, including:
 - Scale data for waste disposed at Ordot Dump
 - GEDA confirmation that grant portion of USDA loan/grant will not materialize since project savings is greater than grant amount
 - GEDA confirmation that GovGuam contribution under USDA loan/grant is fixed at \$39,874,646 and will not decline proportionally to USDA assistance
 - Allocation added to reserve for closure cost of landfill gas collection system
 - Updated information for cost of commercial transfer station



Gershman, Brickner & Bratton, Inc.

70





Guam SOLID WASTE RECEIVER

Preliminary Rate Updated Recommendations for PUC



Customer Type	100% Bond Financing (2009A Section 30)		USDA and Bond Financing (2009A Section 30)	
	Without Military	With Military	Without Military	With Military
Commercial (per ton)	\$177.00	\$142.00	\$164.00	\$131.00
Residential (per month)	\$32.00	\$27.00	\$30.00	\$25.00

Note: Self-haul rates remain the same as previously recommended.



Gershman, Brickner & Bratton, Inc.

71





Guam SOLID WASTE RECEIVER

Interim Rates



- July 1: Third phase of commercial interim rates took effect - \$156 per ton
- July 1: Interim residential rates increased to \$17

Effective Date	Rate/month
July 1, 2010	\$ 17.00
January 1, 2011	\$ 24.00
July 1, 2011	\$ 30.00



Gershman, Brickner & Bratton, Inc.


72

Guam SOLID WASTE RECEIVER



Bridges and Roadway Repairs and Replacements

- June 7: Receiver filed report expressing concern about completion schedule for bridges and road repairs
- DPW revised schedule is tight given planned opening of landfill in mid-2011
- High risk of further delay
- DPW should put contracts in place to minimize delays



Gershman, Brickner & Bratton, Inc.

73


Guam SOLID WASTE RECEIVER

Volume of Waste

First Full Year of Scale Data

Actual Solid Waste Delivered to the Ordot Dump
June 1, 2009 through May 29, 2010

Customer Type	Tons	Percent
Commercial Customers	52,220	65%
Residential Customers	19,412	24%
Transfer Stations	5,114	6%
Mayors	1,392	2%
Government of Guam	2,362	3%
Total	80,501	100%



Gershman, Brickner & Bratton, Inc.

74



Guam SOLID WASTE RECEIVER

Military Participation

- Key to lower and stable long-term rates
- Receiver met with representatives of the Governor's office and the Military
- July 20: Receiver received comments and suggested changes to draft agreement from the Office of the Attorney General
- We will continue to work with all parties



SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.

75



Guam SOLID WASTE RECEIVER



7. NEXT STEPS



SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.


76



Guam SOLID WASTE RECEIVER



Construction, Design and Permitting

- Continue Layon Landfill and Access Road construction management oversight to include all new construction
- Continue to push all project schedule activities to meet deadlines
- Continue Baseline Groundwater Monitoring Plan oversight of monthly monitoring and reporting for preparation of draft Detection Monitoring Plan
- Continue Inarajan oversight and coordination with GWA to install monitoring systems and start marine monitoring activities
- Work to revise and finalize scope of work for Ordut Dump Closure RFP to incorporate EPA and GEPA guidance and issue RFP



Gershman, Brickner & Bratton, Inc.


77



Guam SOLID WASTE RECEIVER



SWMD Operations

- Continue to refine the billing system for SWMD customers, tightening checks and balances on billing and implementing stronger internal auditing processes
- Continue planning for a curbside recycling pilot program
- Continue planning for the collection program for metallic and bulk items, including procuring trucks and planning staffing allocation



Gershman, Brickner & Bratton, Inc.


78



Guam SOLID WASTE RECEIVER



Financial and Capital Funding

- Carefully manage the Citibank Trustee Accounts and keep all parties informed
- Continue to carefully monitor expenditures and revenue collections
- Carefully monitor the volume of waste and update rate information accordingly
- Manage the contracts required to complete the Consent Decree projects
- Continue implementation of the interim rates approved by the Court
- Implement policies to assure that delinquent accounts are paid in full or service is terminated



Gershman, Brickner & Bratton, Inc.


79



Guam SOLID WASTE RECEIVER

Financial and Capital Funding (cont'd)

- Monitor the cleanup of the DPW Compound, manage payments to the contractor and seek reimbursement as ordered by the Court;
- Submit a formal rate request to the Public Utilities Commission
- Continue to advance the long-term agreement with the Military
- Advance procurement activity for the services of a Commercial Transfer Station, an Operator of the Layon Landfill, and for closure of the Ordot Dump



Gershman, Brickner & Bratton, Inc.

80

Guam SOLID WASTE RECEIVER

GBB
SOLID WASTE
MANAGEMENT
CONSULTANTS

Gershman, Brickner & Bratton, Inc.

81
